Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	04 March 2026
Team ID	GACSE-145
Project Name	AI Financial Advisor
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

product backlog and sprint schedule

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Foundation & Setup	USN-1	Set up the Python environment, install Streamlit, and configure the .env for Gemini API keys.	3	High	Kushwaha Rajat Kamalakant
Sprint-1	User Access	USN-2	As a user, I can securely log into the dashboard using local data storage/SQLite.	2	High	Dev Kumar
Sprint-2	Budgeting Core	USN-3	As a user, I can enter expenses to see auto-categorization and receive budget alerts.	5	High	Harsh Chaudhary

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-2	Analysis Logic	USN-4	Develop the financial computation module to calculate savings and debt ratios.	3	Medium	Dev Kumar
Sprint-3	AI Advice Engine	USN-5	Integrate the Gemini API to provide explainable financial Q&A and reasoning.	8	High	Kartikey Singh
Sprint-3	Investment Module	USN-6	As a user, I can get ETF/Mutual Fund suggestions based on my risk profile.	5	Medium	Harsh Chaudhary
Sprint-4	Visualization	USN-7	Generate dynamic charts (Matplotlib/Seaborn) for the financial health dashboard.	3	Medium	Dev Kumar
Sprint-4	Deployment	USN-8	Complete README, user manual, and deploy the application for final submission.	2	High	Team Leader

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Start Date	Planned End Date	Status
Sprint-1	5	7 Days	10 Feb 2026	17 Feb 2026	Completed
Sprint-2	8	7 Days	18 Feb 2026	24 Feb 2026	Completed
Sprint-3	13	7 Days	25 Feb 2026	03 Mar 2026	Completed
Sprint-4	5	5 Days	04 Mar 2026	08 Mar 2026	**In Progress**

Velocity:
Imagine we have a 10-day sprint duration, and the velocity of the team is 20 (points per sprint). Let's calculate the team's average velocity (AV) per iteration unit (story points per day)

$$AV = \frac{sprint\ duration}{velocity} = \frac{20}{10} = 2$$

$$AV = \frac{\text{Total Story Points (31)}}{\text{Total Duration (26 Days)}} = 1.19 \text{ points/day}$$

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum. However, burn down charts can be applied to any project containing measurable progress over time.

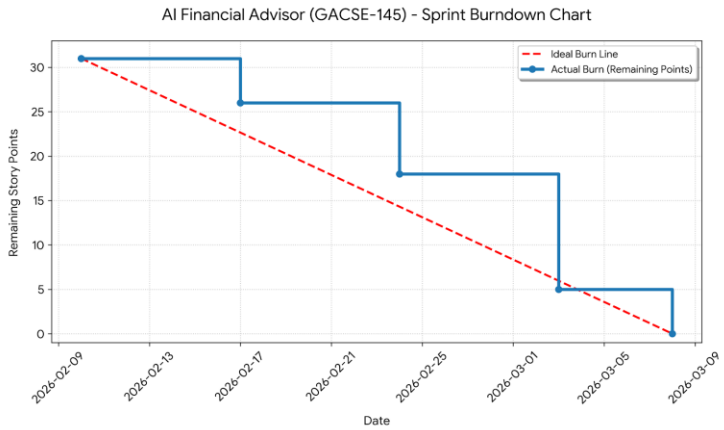

https://www.visual-paradigm.com/scrum/scrum-burndown-chart/

https://www.atlassian.com/agile/tutorials/burndown-charts
